

OK G/wm



ENGINEERS JOINT CONTRACT  
DOCUMENTS COMMITTEE

# Contractor's Application for Payment No.

SIX (6)

|                                      |                                                    |                                                 |
|--------------------------------------|----------------------------------------------------|-------------------------------------------------|
| To<br>(Owner): CITY OF VICKSBURG     | Application<br>Period: 11/01/2017 to 11/30/2017    | Application Date: 12/8/2017                     |
| Project: NEW PRIMARY CLARIFIER NO. 1 | From (Contractor): T.L. WALLACE CONSTRUCTION, INC. | Via (Engineer): ENGINEERING SERVICE             |
| Owner's Contract No.:                | Contract:                                          | Engineer's Project No.: CDBG #1131-14-374-PF-01 |
|                                      | Contractor's Project No.: WAR7514                  |                                                 |

## Application For Payment Change Order Summary

| Approved Change Orders |           |            | 1. ORIGINAL CONTRACT PRICE.....                                | \$ 1,609,935.00 |
|------------------------|-----------|------------|----------------------------------------------------------------|-----------------|
| Number                 | Additions | Deductions | 2. Net change by Change Orders.....                            | \$              |
| 1                      |           |            | 3. Current Contract Price (Line 1 ± 2).....                    | \$ 1,609,935.00 |
|                        |           |            | 4. TOTAL COMPLETED AND STORED TO DATE                          |                 |
|                        |           |            | (Column F on Progress Estimate).....                           | \$ 969,486.05   |
|                        |           |            | 5. RETAINAGE:                                                  |                 |
|                        |           |            | a. 5% X \$946,822.50 Work Completed.....                       | \$ 47,341.13    |
|                        |           |            | b. 5% X \$22,663.55 Stored Material.....                       | \$ 1,133.18     |
|                        |           |            | c. Total Retainage (Line 5a + Line 5b).....                    | \$ 48,474.30    |
|                        |           |            | 6. AMOUNT ELIGIBLE TO DATE (Line 4 - Line 5c).....             | \$ 921,011.75   |
|                        |           |            | 7. LESS PREVIOUS PAYMENTS (Line 6 from prior Application)..... | \$ 815,809.79   |
|                        |           |            | 8. AMOUNT DUE THIS APPLICATION.....                            | \$ 105,201.96   |
|                        |           |            | 9. BALANCE TO FINISH, PLUS RETAINAGE                           |                 |
|                        |           |            | (Column G on Progress Estimate + Line 5 above).....            | \$ 688,923.25   |
| TOTALS                 |           |            |                                                                |                 |
| NET CHANGE BY          |           |            |                                                                |                 |
| CHANGE ORDERS          |           |            |                                                                |                 |

### Contractor's Certification

The undersigned Contractor certifies that to the best of its knowledge: (1) all previous progress payments received from Owner on account of Work done under the Contract have been applied on account to discharge Contractor's legitimate obligations incurred in connection with Work covered by prior Applications for Payment; (2) title of all Work, materials and equipment incorporated in said Work or otherwise listed in or covered by this Application for Payment will pass to Owner at time of payment free and clear of all Liens, security interests and encumbrances (except such as are covered by a Bond acceptable to Owner indemnifying Owner against any such Liens, security interest or encumbrances); and (3) all Work covered by this Application for Payment is in accordance with the Contract Documents and is not defective.

By:

*Joey Reagan*

Date:

12-11-17

Payment of:

\$ 105,201.96

(Line 8 or other - attach explanation of the other amount)

is recommended by:

*Jimmy K. Dutton*  
(Engineer)

12/13/17  
(Date)

Payment of:

\$ 105,201.96

(Line 8 or other - attach explanation of the other amount)

is approved by:

George Flaggs (Owner) Mayor

1/16/2018

(Date)

Approved by:

*Guay M. Ortiz*  
Funding Agency (if applicable)

1/9/2018  
(Date)

# Progress Estimate - Unit Price Work

# Contractor's Application

| For (Contract): NEW PRIMARY CLARIFIER NO. 1  |                                                        |                   |              |                       |                              |                                 | Application Number: SLX (6)           |                                            |              |                           |
|----------------------------------------------|--------------------------------------------------------|-------------------|--------------|-----------------------|------------------------------|---------------------------------|---------------------------------------|--------------------------------------------|--------------|---------------------------|
| Application Period: 11/01/2017 to 11/30/2017 |                                                        |                   |              |                       |                              |                                 | Application Date: 12/8/2017           |                                            |              |                           |
| A                                            |                                                        |                   |              | B                     | C                            | D                               | E                                     | F                                          |              |                           |
| Item                                         |                                                        | Bid Item Quantity | Unit Price   | Bid Item Value (\$)   | Estimated Quantity Installed | Value of Work Installed to Date | Materials Presently Stored (not in C) | Total Completed and Stored to Date (D + E) | % (F / B)    | Balance to Finish (B - F) |
| Bid Item No.                                 | Description                                            |                   |              |                       |                              |                                 |                                       |                                            |              |                           |
| 1.0                                          | MOBILIZATION                                           | 1                 | \$75,000.00  | \$75,000.00           | 0.7                          | \$52,500.00                     |                                       | \$52,500.00                                | 70.0%        | \$22,500.00               |
| 2.0                                          | DEMOLITION (PC #1)                                     | 1                 | \$100,000.00 | \$100,000.00          | 1                            | \$100,000.00                    |                                       | \$100,000.00                               | 100.0%       |                           |
| 3.0                                          | DEMOLITION (PC #2) Effluent Box, Piping, Walks, Etc... | 1                 | \$17,200.00  | \$17,200.00           |                              |                                 |                                       |                                            |              | \$17,200.00               |
| 4.0                                          | CAST-IN-PLACE CONCRETE (PC #1, 4000 PSI)               | 1                 | \$450,000.00 | \$450,000.00          | 0.85                         | \$382,500.00                    | \$2,500.00                            | \$385,000.00                               | 85.6%        | \$65,000.00               |
| 5.0                                          | CAST-IN-PLACE CONCRETE (PC #2, Effluent Box, 4000 PSI) | 1                 | \$25,000.00  | \$25,000.00           |                              |                                 | \$900.00                              | \$900.00                                   | 3.6%         | \$24,100.00               |
| 6.0                                          | CAST-IN-PLACE CONCRETE (Stairs, 3000 PSI)              | 1                 | \$15,000.00  | \$15,000.00           |                              |                                 | \$200.00                              | \$200.00                                   | 1.3%         | \$14,800.00               |
| 7.0                                          | CAST-IN-PLACE CONCRETE (Walks, Paving, Misc, 3000 PSI) | 1                 | \$20,700.00  | \$20,700.00           |                              |                                 | \$225.00                              | \$225.00                                   | 1.1%         | \$20,475.00               |
| 8.0                                          | GROUT (PC #1 Bottom, 2" Thickness)                     | 1                 | \$27,500.00  | \$27,500.00           |                              |                                 |                                       |                                            |              | \$27,500.00               |
| 9.0                                          | GROUT (PC #1 Trough)                                   | 1                 | \$15,900.00  | \$15,900.00           |                              |                                 |                                       |                                            |              | \$15,900.00               |
| 10.0                                         | GROUT (Effluent Box #1 & #2)                           | 1                 | \$9,200.00   | \$9,200.00            |                              |                                 |                                       |                                            |              | \$9,200.00                |
| 11.0                                         | FLOWABLE FILL                                          | 1                 | \$16,200.00  | \$16,200.00           |                              |                                 |                                       |                                            |              | \$16,200.00               |
| 12.0                                         | SLIDE GATE ASSEMBLY (PC #1 & #2)                       | 2                 | \$8,050.00   | \$16,100.00           |                              |                                 | \$9,076.00                            | \$9,076.00                                 | 56.4%        | \$7,024.00                |
| 13.0                                         | HANDRAIL, ALUMINUM (PC #1 Perimeter)                   | 1                 | \$14,000.00  | \$14,000.00           |                              |                                 |                                       |                                            |              | \$14,000.00               |
| 14.0                                         | HANDRAIL (Stairs) ALUMINUM                             | 1                 | \$2,925.00   | \$2,925.00            |                              |                                 |                                       |                                            |              | \$2,925.00                |
| 15.0                                         | GRATINGS, STAINLESS (PC #1 & #2)                       | 1                 | \$7,400.00   | \$7,400.00            |                              |                                 |                                       |                                            |              | \$7,400.00                |
| 16.0                                         | INFLUENT PS WET WELL CLEANING & BY-PASSING             | 1                 | \$38,450.00  | \$38,450.00           |                              |                                 |                                       |                                            |              | \$38,450.00               |
| 17.0                                         | H-STEEL PILE LOAD TEST                                 | 1                 | \$32,120.00  | \$32,120.00           | 1                            | \$32,120.00                     |                                       | \$32,120.00                                | 100.0%       |                           |
| 18.0                                         | HP 12x53 STEEL PILES                                   | 61                | \$3,150.00   | \$192,150.00          | 61                           | \$192,150.00                    |                                       | \$192,150.00                               | 100.0%       |                           |
| 19.0                                         | SITE WORK (PC #1)                                      | 1                 | \$43,950.00  | \$43,950.00           | 0.75                         | \$32,962.50                     |                                       | \$32,962.50                                | 75.0%        | \$10,987.50               |
| 20.0                                         | SITE WORK (PC #2)                                      | 1                 | \$7,320.00   | \$7,320.00            |                              |                                 |                                       |                                            |              | \$7,320.00                |
| 21.0                                         | SELECT FILL - GENERAL, IMPORTED                        | 1                 | \$6,900.00   | \$6,900.00            |                              |                                 |                                       |                                            |              | \$6,900.00                |
| 22.0                                         | SELECT FILL - GRANULAR, IMPORTED                       | 1                 | \$29,500.00  | \$29,500.00           | 0.45                         | \$13,275.00                     |                                       | \$13,275.00                                | 45.0%        | \$16,225.00               |
| 23.0                                         | SELECT FILL - DRAINAGE BLANKET                         | 1                 | \$8,850.00   | \$8,850.00            | 1                            | \$8,850.00                      |                                       | \$8,850.00                                 | 100.0%       |                           |
| 24.0                                         | SELECT FILL - PLATING, IMPORTED                        | 1                 | \$14,550.00  | \$14,550.00           |                              |                                 |                                       |                                            |              | \$14,550.00               |
| 25.0                                         | TEMPORARY SILT FENCE                                   | 1                 | \$2,100.00   | \$2,100.00            | 0.75                         | \$1,575.00                      |                                       | \$1,575.00                                 | 75.0%        | \$525.00                  |
| 26.00                                        | TEMPORARY EROSION CONTROL CHECKS                       | 1                 | \$1,600.00   | \$1,600.00            | 0.75                         | \$1,200.00                      |                                       | \$1,200.00                                 | 75.0%        | \$400.00                  |
| 27.00                                        | SWPPP MAINTENANCE                                      | 1                 | \$1,800.00   | \$1,800.00            | 0.75                         | \$1,350.00                      |                                       | \$1,350.00                                 | 75.0%        | \$450.00                  |
| 28.00                                        | SITE RESTORATION                                       | 1                 | \$3,250.00   | \$3,250.00            |                              |                                 |                                       |                                            |              | \$3,250.00                |
| 29.0                                         | CLEAN & CCTV 24" CIP                                   | 1                 | \$670.00     | \$670.00              |                              |                                 |                                       |                                            |              | \$670.00                  |
| 30.0                                         | CLEAN & CCTV 6" CIP                                    | 1                 | \$1,900.00   | \$1,900.00            |                              |                                 |                                       |                                            |              | \$1,900.00                |
| <b>Totals</b>                                |                                                        |                   |              | <b>\$1,197,235.00</b> |                              | <b>\$818,482.50</b>             | <b>\$12,901.00</b>                    | <b>\$831,383.50</b>                        | <b>69.4%</b> | <b>\$365,851.50</b>       |

## Contractor's Application

EJCDC C-620 Contractor's Application for Payment  
© 2010 National Society of Professional Engineers for EJCDC. All rights reserved.  
Page 3 of 4

## Stored Material Summary

## Contractor's Application

[illegible]

4025 Highway 35 North  
Columbia, MS 39429



(601) 736-4525 Office  
(601) 736-3401 Fax

December 7, 2017

## MONTHLY NARRATIVE REPORT

|                     |                               |                  |                     |
|---------------------|-------------------------------|------------------|---------------------|
| Project Name:       | New Primary Clarifier #1      | Professional:    | Engineering Service |
| Location:           | Wastewater Treatment Facility | Owner:           | City of Vicksburg   |
| Date:               | Period to October 31, 2017    | Project Supt:    | Bobby Carter        |
| CDBG Project #      | 1131-14-374-PF-01             | Contractor Job#: | WAR7514             |
| Project Start Date: | 5/22/2017                     | Completion Date: | 2/16/2018           |

### 1. Activities completed during this reporting period:

- Installed of French drain system at Clarifier #1
- Backfilling (above French drain to subgrade trench concrete)
- Form & pour trench bottom

#### Activities in progress during this reporting period:

- Form & pour trench bottom & outside walls

#### Activities schedule next reporting period:

- Current schedule is attached
- Backfilling
- Clarifier #1 Equipment installation
- Slide Gate Installation Clarifier #1

### 2. Description of any problem areas:

- None at this time

### 3. Current & anticipated delays:

- a. Cause of delay
- b. Corrective action & schedule adjustments to correct the delay.
- c. Impact of the delay on other activities, milestones & completion dates - Schedule attached

### 4. Change in project sequence:


- None



**TLW**  
alliance  
Construction, Inc.

# Construction, Inc.

10. Other:

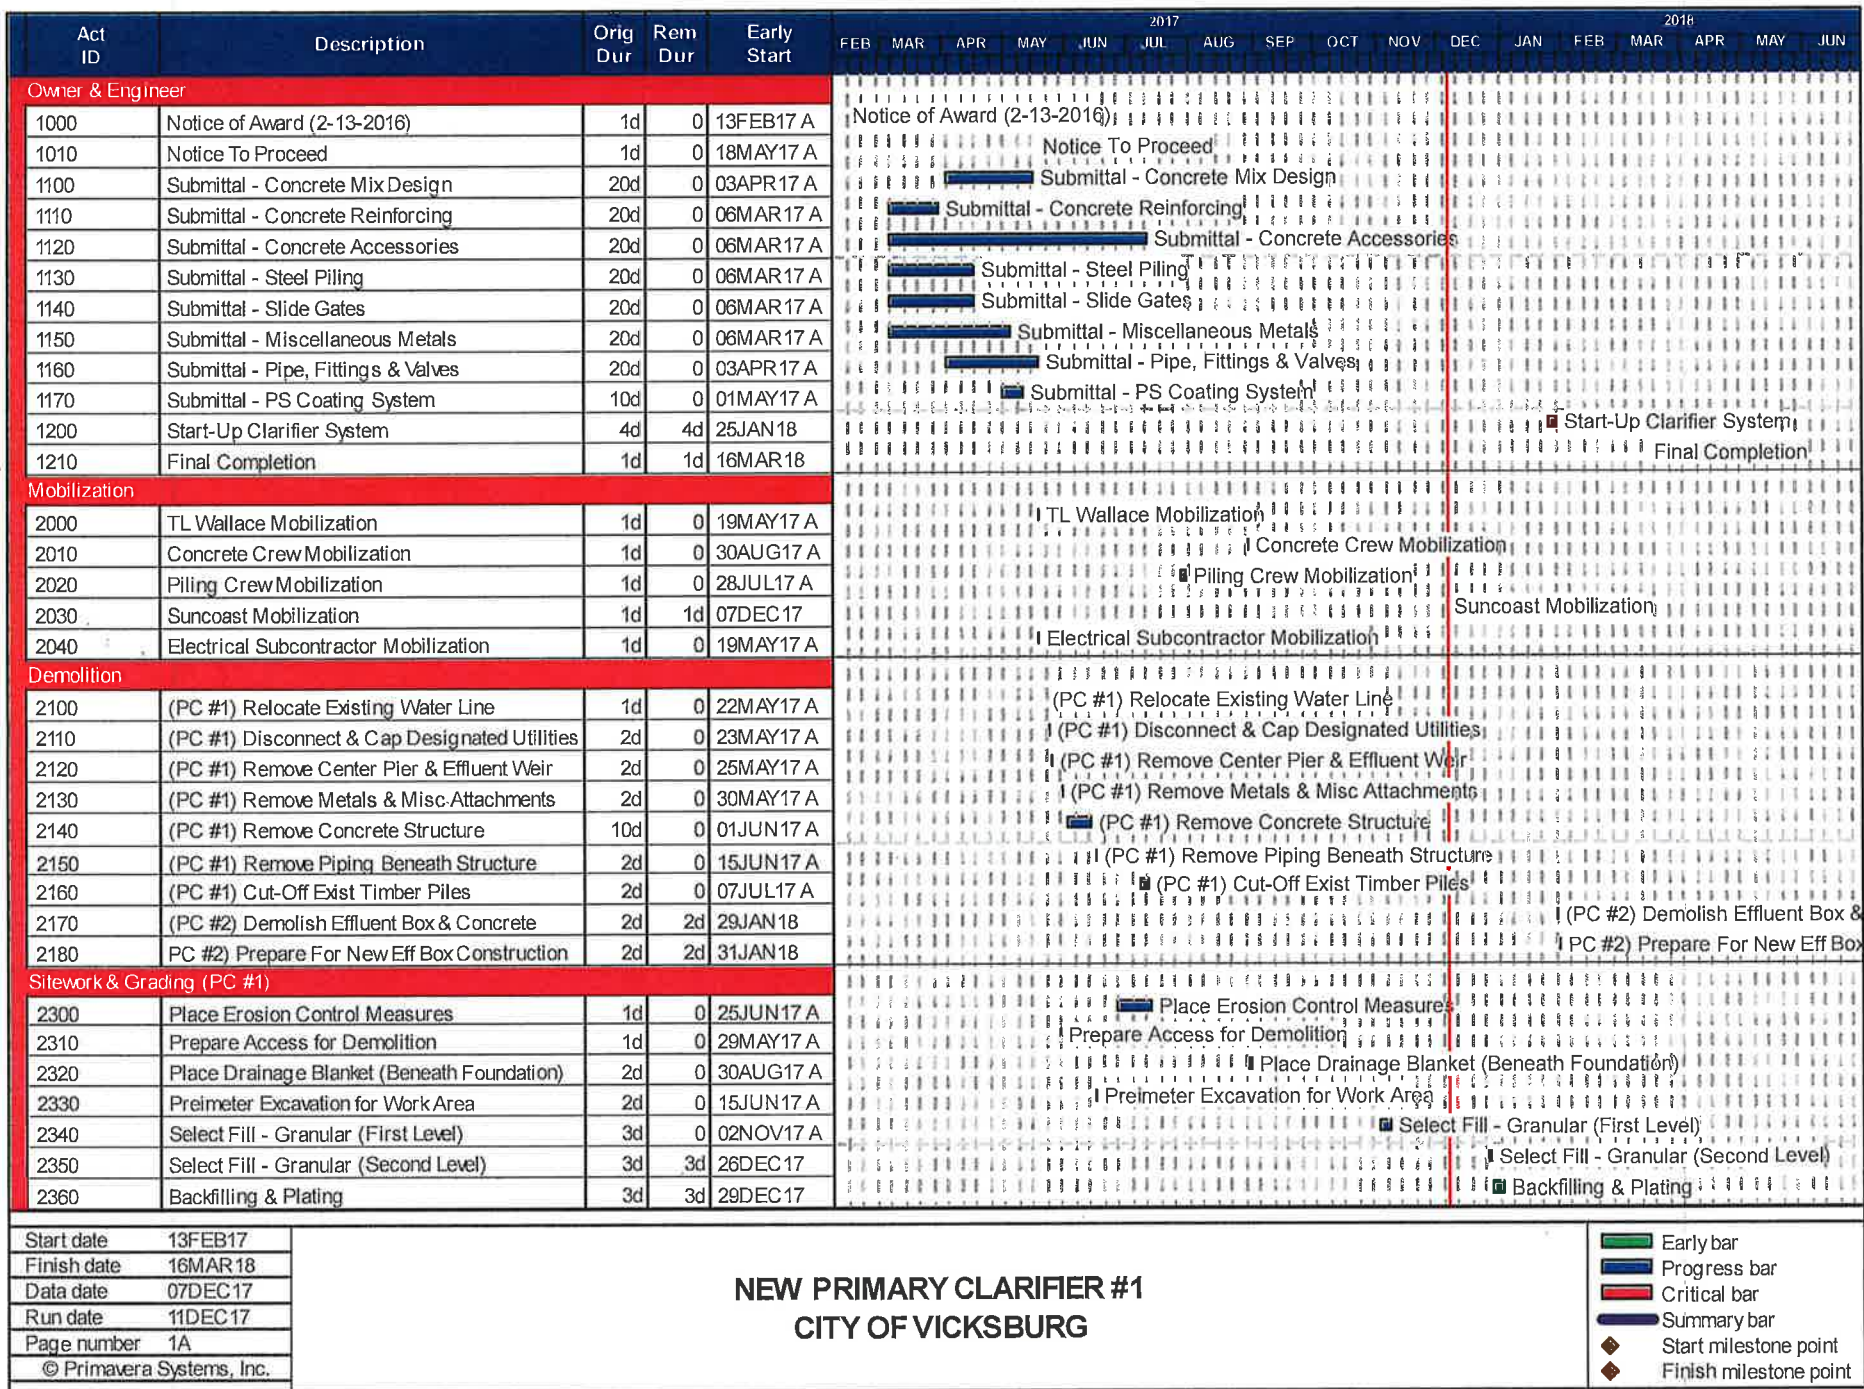

| Act ID | Description      | Orig Dur | Rem Dur | Early Start | 2017 |     |     |     |     |     |     |     |     |     |     |     | 2018 |     |     |     |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|--------|------------------|----------|---------|-------------|------|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|------|-----|-----|-----|-----|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
|        |                  |          |         |             | FEB  | MAR | APR | MAY | JUN | JUL | AUG | SEP | OCT | NOV | DEC | JAN | FEB  | MAR | APR | MAY | JUN |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 2370   | Site Restoration | 2d       | 2d      | 15JAN18     |      |     |     |     |     |     |     |     |     |     |     |     |      |     |     |     |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |

